SINK WALL ELEVATION

SOURCE COORDINATION / 22 OCT 2026

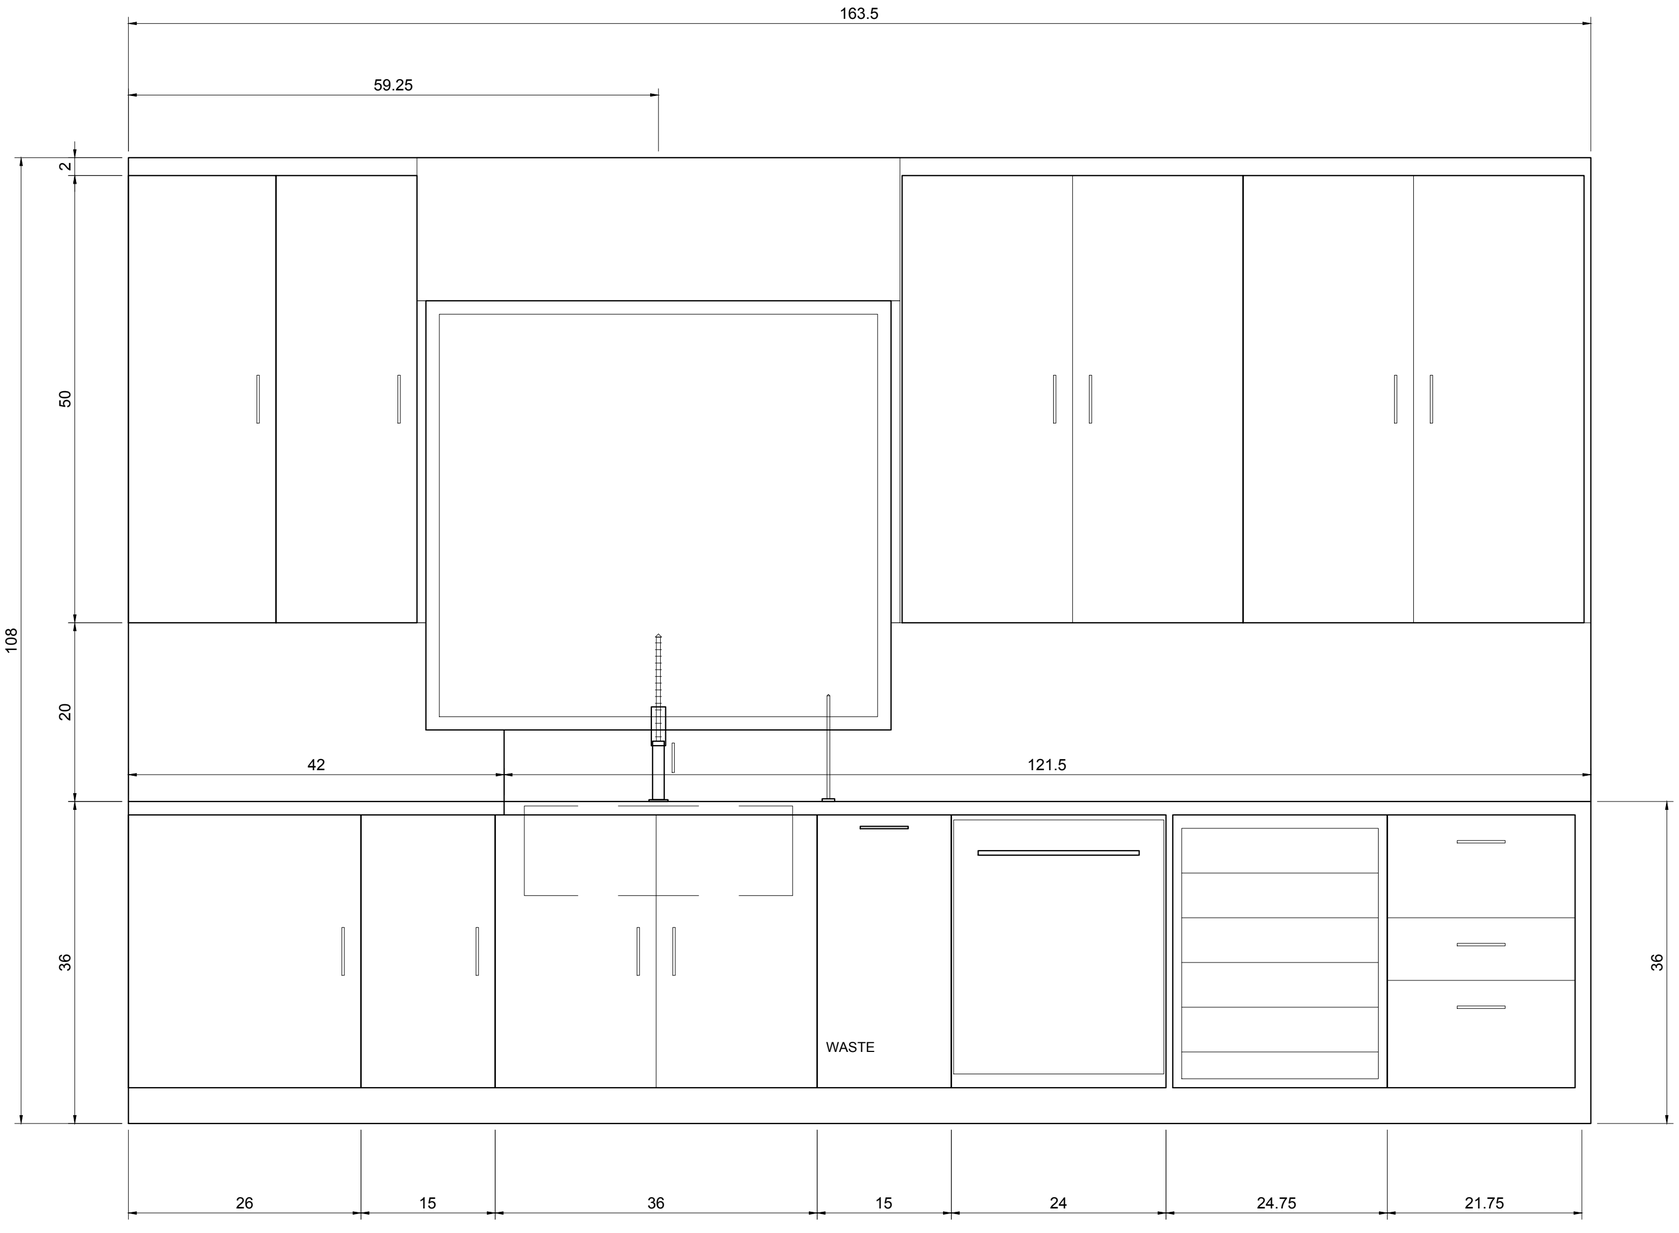

COUNTER / BACKSPLASH
Base run 162.5; finished counter 163.5.
C03 and B06 each 121.5 long.
Counter and backsplash seams at 42.
B06 continuous shaped piece.

WINDOW / SINK HOLD
Window / sink / tap CL = 59.25
from back-wall drywall, nominal.
Cabinet p. 6 flags 1/4 in. discrepancy.
Resolve before sink or tap machining.
Blinds and internal applied trim removed.
W01-W07: seven porcelain pieces.

PROPOSED FIXTURES
Kraus KWU110-30 sink study.
KPF1610 current study: 18.75 high.
8.625 reach / 6.25 outlet above deck.
Separate filter tap to the right.
Final cutout templates and tap offsets
must follow selected products.

OTHER HOLDS
15 in. full-height waste pullout.
Tandem garbage / recycling bins.
Internal divider/support; see A402.
Final bin/hardware selection pending.
Counter seam-to-cutout gap: field check.
123 slab - 121.5 piece = 1.5 gross
before kerf, edge and trim allowances.

SOURCE
Cabinet p. 6; R9 S03 / S04 / S10.

02 SINK WALL / ALIGNED STONE SEAM

Window width 52 nominal; sill 44 and head 92 are retained study levels, subject to field template.
